


Crozet Master Plan Update

2020 Work & Engagement Plan (COVID Revision)

If no additional work sessions are needed, this timeline projects plan adoption as early as March 2021. The original targeted completion date for this project was Q4 2020 (15 months).

DRAFT
April 21, 2020

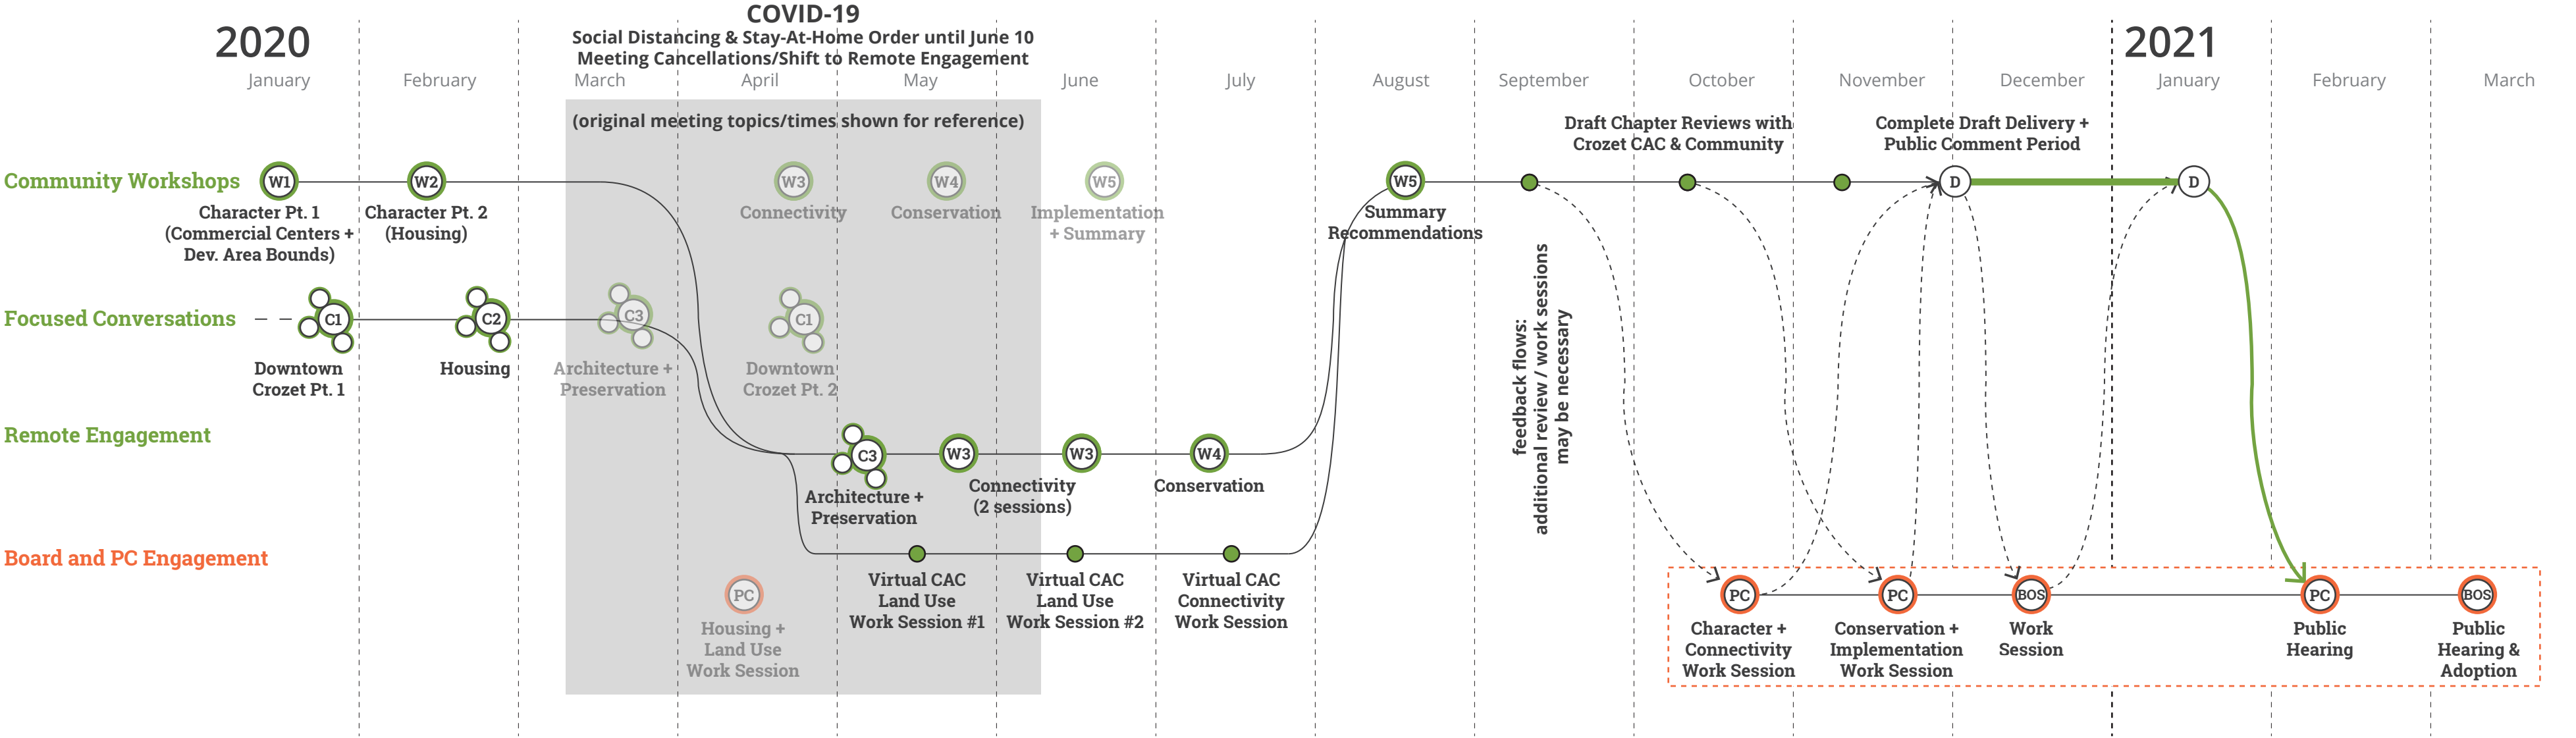

Summary of Schedule Changes

- W3 Connectivity Workshop**
Originally scheduled for April 22, will be broken into two remote sessions. Session #1 will focus on bicycle and pedestrian connectivity, including trails. Session #2 will focus on vehicular connectivity and transit.
- W4 Conservation Workshop**
Originally scheduled for May 27. This workshop will focus on parks and greenways and sustainability topics including climate action, tree canopy, dark skies, viewsheds, etc.
- W5 Summary Recommendations Workshop**
Originally scheduled for June 24 and could also be postponed to such time that in-person engagement is practicable. This workshop is intended to provide an opportunity for input on draft recommendations and feedback received to date.
- C3 Architecture + Preservation Focused Conversation**
Originally scheduled for March 27, will be adapted to an online questionnaire.
- C1 Downtown Crozet Focused Conversation**
This second Downtown Crozet Focused Conversation will be cancelled. This meeting was intended to provide an opportunity for public comment on findings from the ongoing market and parking studies, with presentations from external consultants. As no date/time was selected and these studies are still forthcoming, staff recommends cancelling this conversation.
- Draft Chapter Reviews / Check-Ins with Crozet CAC**
Many of these check-ins have been delayed due to time demands from rezoning and special use permit community meetings. There are additional difficulties with digital meetings due to the requirements of the Virginia Freedom of Information Act. Work sessions and check-ins with the CAC have been postponed to provide time for staff to continue to collect essential community input and allow the CAC to review draft chapters and recommendations in late summer/early fall.

- D Draft Master Plan Delivery**
Opportunities for public comment and engagement will be provided in conjunction with releases of the completed draft Master Plan. Two major drafts are anticipated, with additional revisions to take place between draft releases and public hearings. Draft chapters and content will be released for public comment and review by the Crozet CAC and Planning Commission on a rolling basis.
- BOS Work Sessions & Public Hearings**
The scope and number of planning work sessions may vary depending on the degree of community feedback and consensus around plan recommendations. If there are a large number of contentious items, these work sessions may need to be pushed back or additional work sessions added, pushing back the plan's adoption. It is possible the dynamics of online engagement may pose difficulties for consensus-building dialogue and creating community buy-in around the Master Plan. However, these impacts are not known at this time.
